


FARR LAKE/DANUBE POND DREDGING PROJECT

Change Order No 1



MARCH 14, 2022

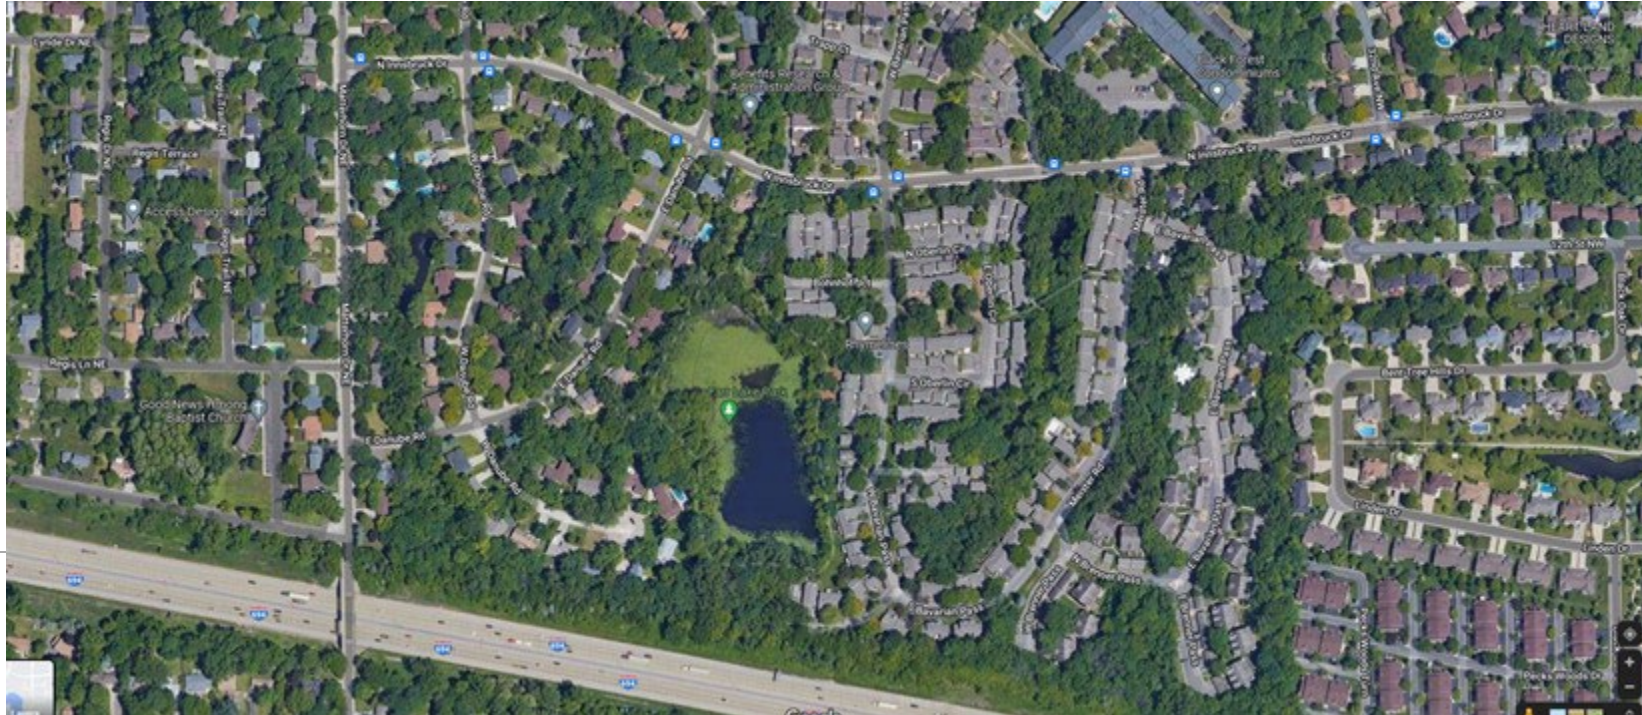


FARR LAKE/DANUBE POND DREDGING PROJECT

- Barr Engineering completed a study of the Farr Lake/Danube Pond area in 2019
- A recommendation of the study was to remove sediment from several ponds and wetlands
- A project was designed to provide pond maintenance and stormwater treatment
- The work is being completed under a contract with Peterson Companies of Chisago City, MN.
- The original contract amount for this project was \$74,228



FARR LAKE/DANUBE POND DREDGING PROJECT

- The Contractor has submitted a pay request in the amount of \$125,755.14
- The additional cost was due to additional sediment in the pond that was directed to be removed, and conditions in one pond substantially different than the other three. The contractor removed all sediment allowed while on site, which will afford additional time until maintenance is required again.
- Change Order No. 1 includes the cost to complete the project including additional directed work. The amount of Change Order 1 is \$ 51,527.14
- Total work included in Change Order No. 1 would increase the original contract by 69%.

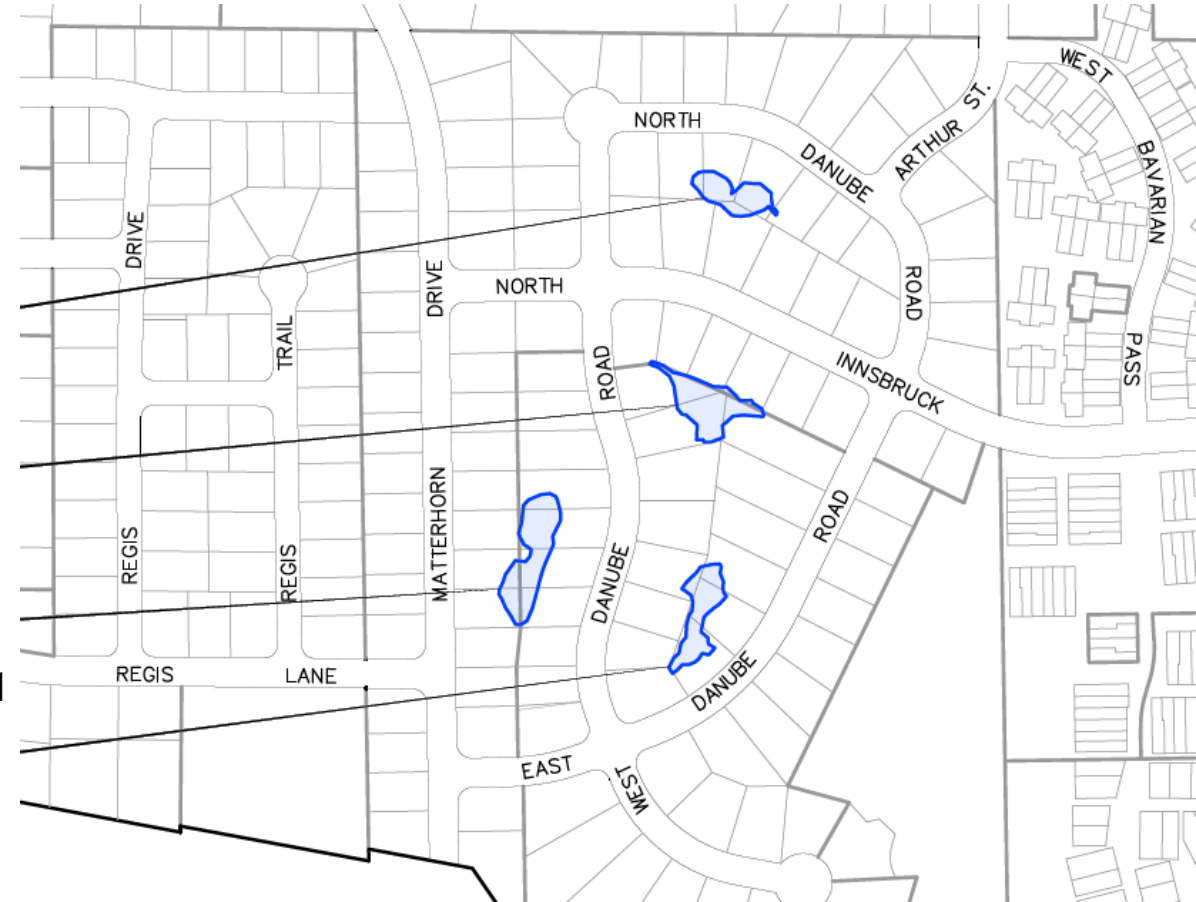

FARR LAKE/DANUBE POND DREDGING PROJECT



FARR LAKE/DANUBE POND DREDGING PROJECT



FARR LAKE/DANUBE POND DREDGING PROJECT



FARR LAKE/DANUBE POND DREDGING PROJECT



REQUESTED MOTION

- Staff requests the City Council

move to approve Resolution No. 2022-23 authorizing Change Order 1

found on pages 141 of tonight's agenda
